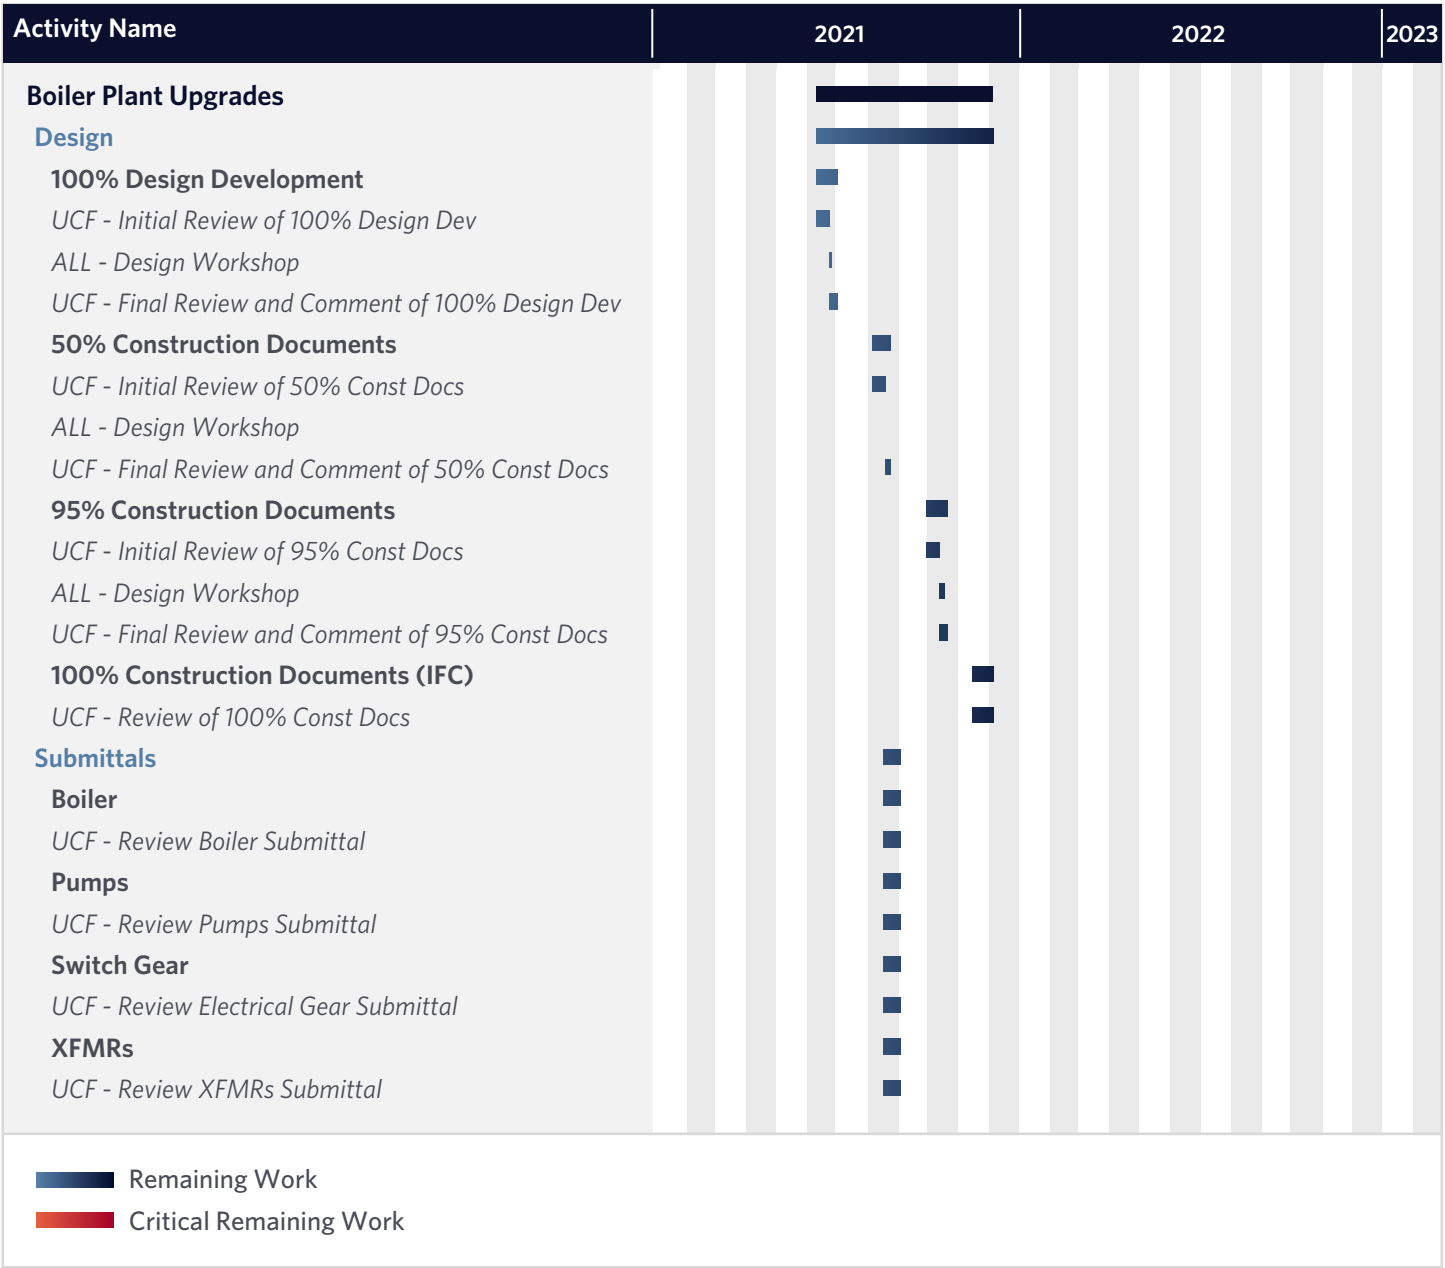
Activity Name
2021
2022
2023
Boiler Plant Upgrades
Design
100% Design Development
UCF - Initial Review of 100% Design Dev
ALL - Design Workshop
UCF - Final Review and Comment of 100% Design Dev
50% Construction Documents
UCF - Initial Review of 50% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 50% Const Docs
95% Construction Documents
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
100% Construction Documents (IFC)
UCF - Review of 100% Const Docs
Submittals
Boiler
UCF - Review Boiler Submittal
Pumps
UCF - Review Pumps Submittal
Switch Gear
UCF - Review Electrical Gear Submittal
XFMRs
UCF - Review XFMRs Submittal
Remaining Work
Critical Remaining Work

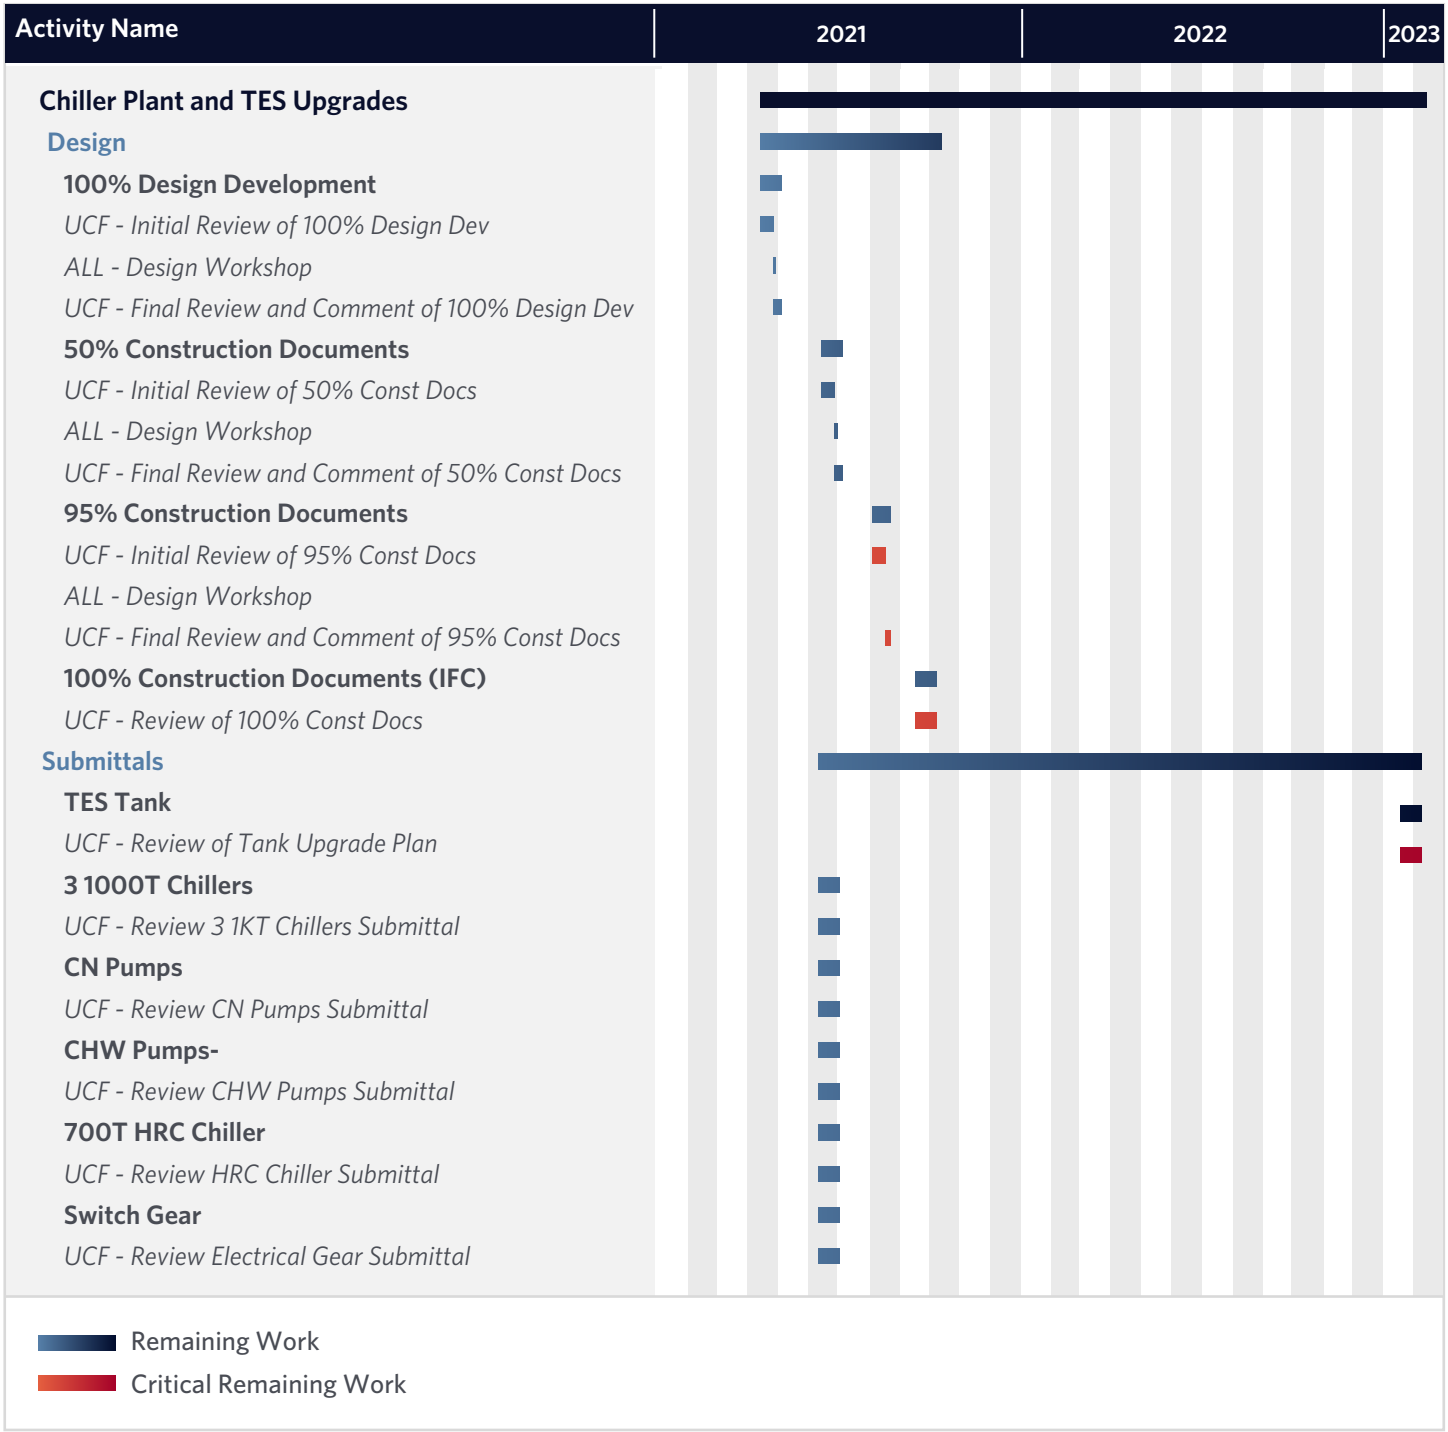
Activity Name
2021
2022
2023
Chiller Plant and TES Upgrades
Design
100% Design Development
UCF - Initial Review of 100% Design Dev
ALL - Design Workshop
UCF - Final Review and Comment of 100% Design Dev
50% Construction Documents
UCF - Initial Review of 50% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 50% Const Docs
95% Construction Documents
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
100% Construction Documents (IFC)
UCF - Review of 100% Const Docs
Submittals
TES Tank
UCF - Review of Tank Upgrade Plan
3 1000T Chillers
UCF - Review 3 1KT Chillers Submittal
CN Pumps
UCF - Review CN Pumps Submittal
CHW Pumps-
UCF - Review CHW Pumps Submittal
700T HRC Chiller
UCF - Review HRC Chiller Submittal
Switch Gear
UCF - Review Electrical Gear Submittal
Remaining Work
Critical Remaining Work

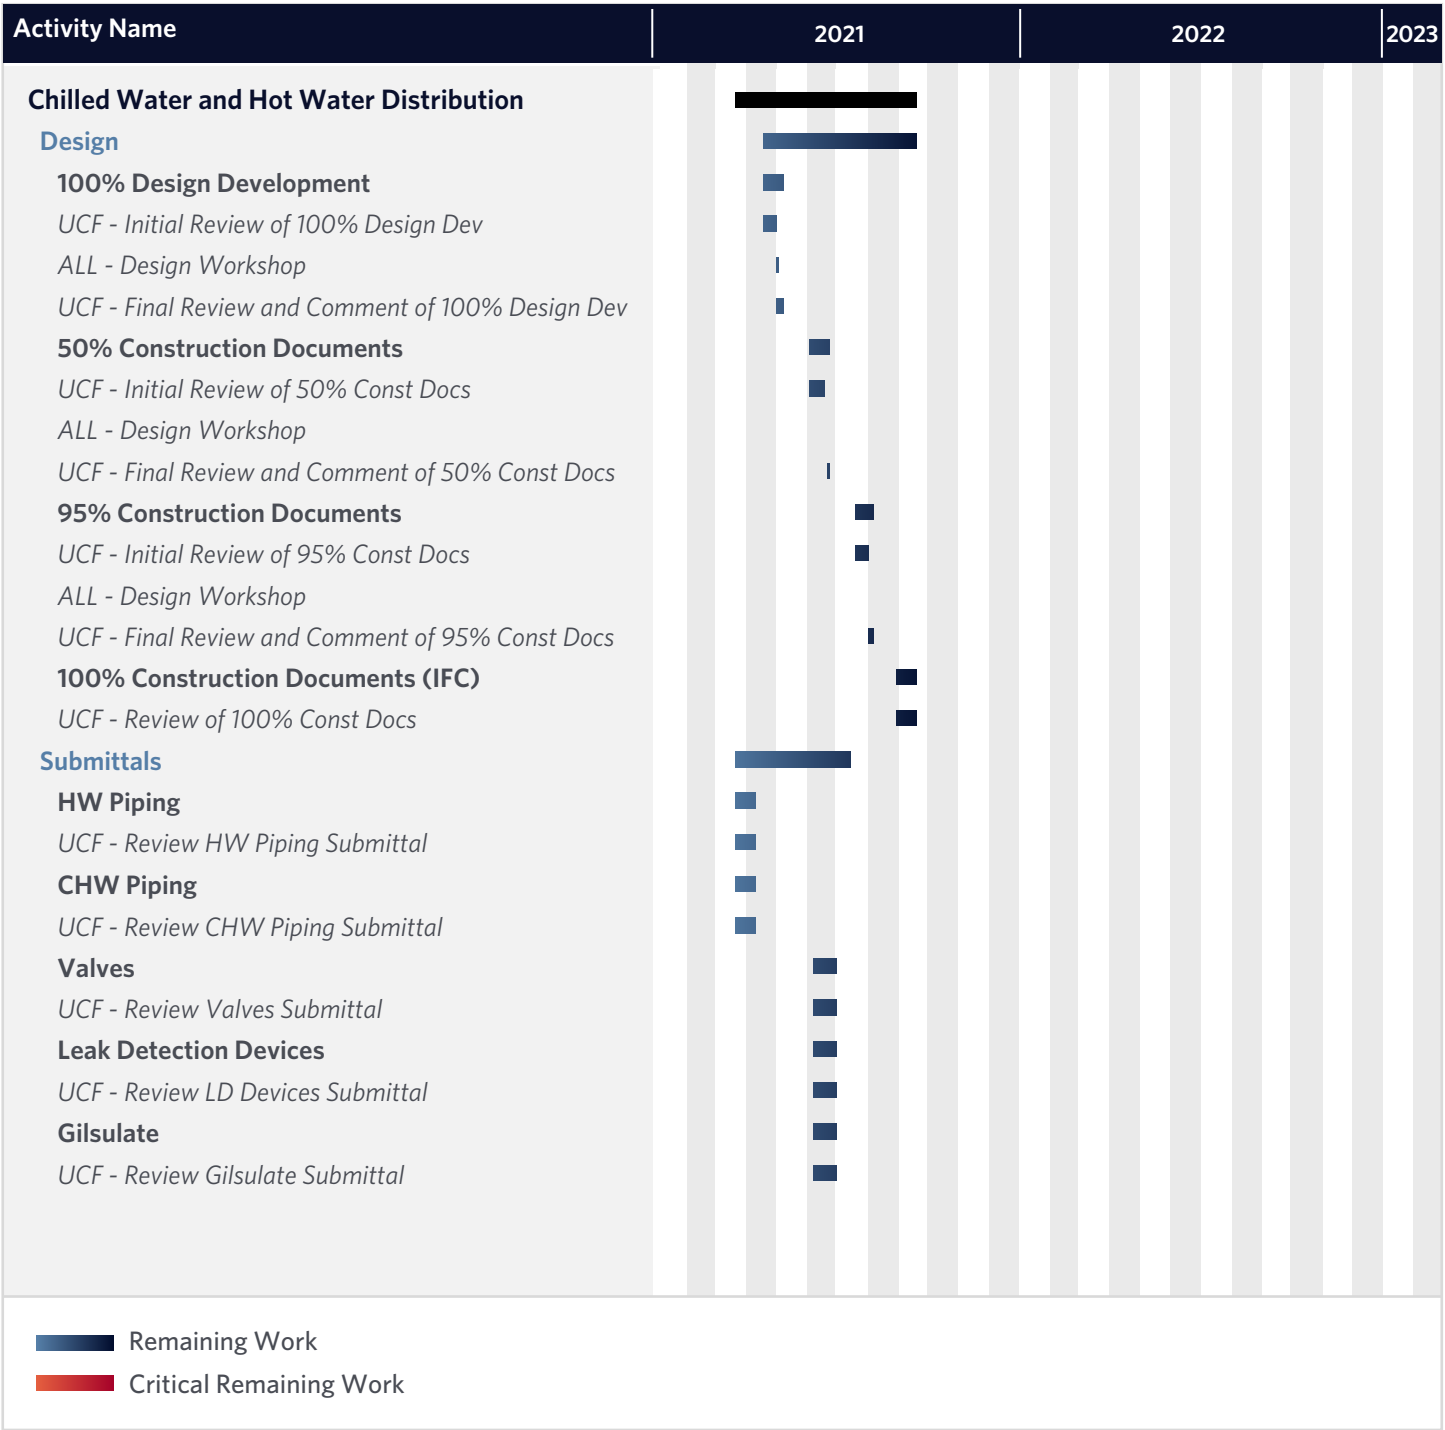
Activity Name
2021
2022
2023
Chilled Water and Hot Water Distribution
Design
100% Design Development
UCF - Initial Review of 100% Design Dev
ALL - Design Workshop
UCF - Final Review and Comment of 100% Design Dev
50% Construction Documents
UCF - Initial Review of 50% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 50% Const Docs
95% Construction Documents
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
100% Construction Documents (IFC)
UCF - Review of 100% Const Docs
Submittals
HW Piping
UCF - Review HW Piping Submittal
CHW Piping
UCF - Review CHW Piping Submittal
Valves
UCF - Review Valves Submittal
Leak Detection Devices
UCF - Review LD Devices Submittal
Gilsulate
UCF - Review Gilsulate Submittal
Remaining Work
Critical Remaining Work

Activity Name	2021	2022	2023
Renewables			
Design			
100% Design Development			
UCF - Initial Review of 100% Design Dev			
ALL - Design Workshop			
UCF - Final Review and Comment of 100% Design Dev			
50% Construction Documents			
UCF - Initial Review of 50% Const Docs			
ALL - Design Workshop			
UCF - Final Review and Comment of 50% Const Docs			
95% Construction Documents			
UCF - Initial Review of 95% Const Docs			
ALL - Design Workshop			
UCF - Final Review and Comment of 95% Const Docs			
100% Construction Documents (IFC)			
UCF - Review of 100% Const Docs			
Submittals			
Light Fixtures			
UCF - Review Light Fixtures Submittal			
480V Panels			
UCF - Review 480V Panel Submittal			
Data Acquisition Unit			
UCF - Review DAU Submittal			
XFMRs			
UCF - Review XFMRs Submittal			
Switch Gear / Substation			
UCF - Review SG/SubS Submittal			
Structural Steel			
UCF - Review Structural Steel Submittal			

Remaining Work

Critical Remaining Work

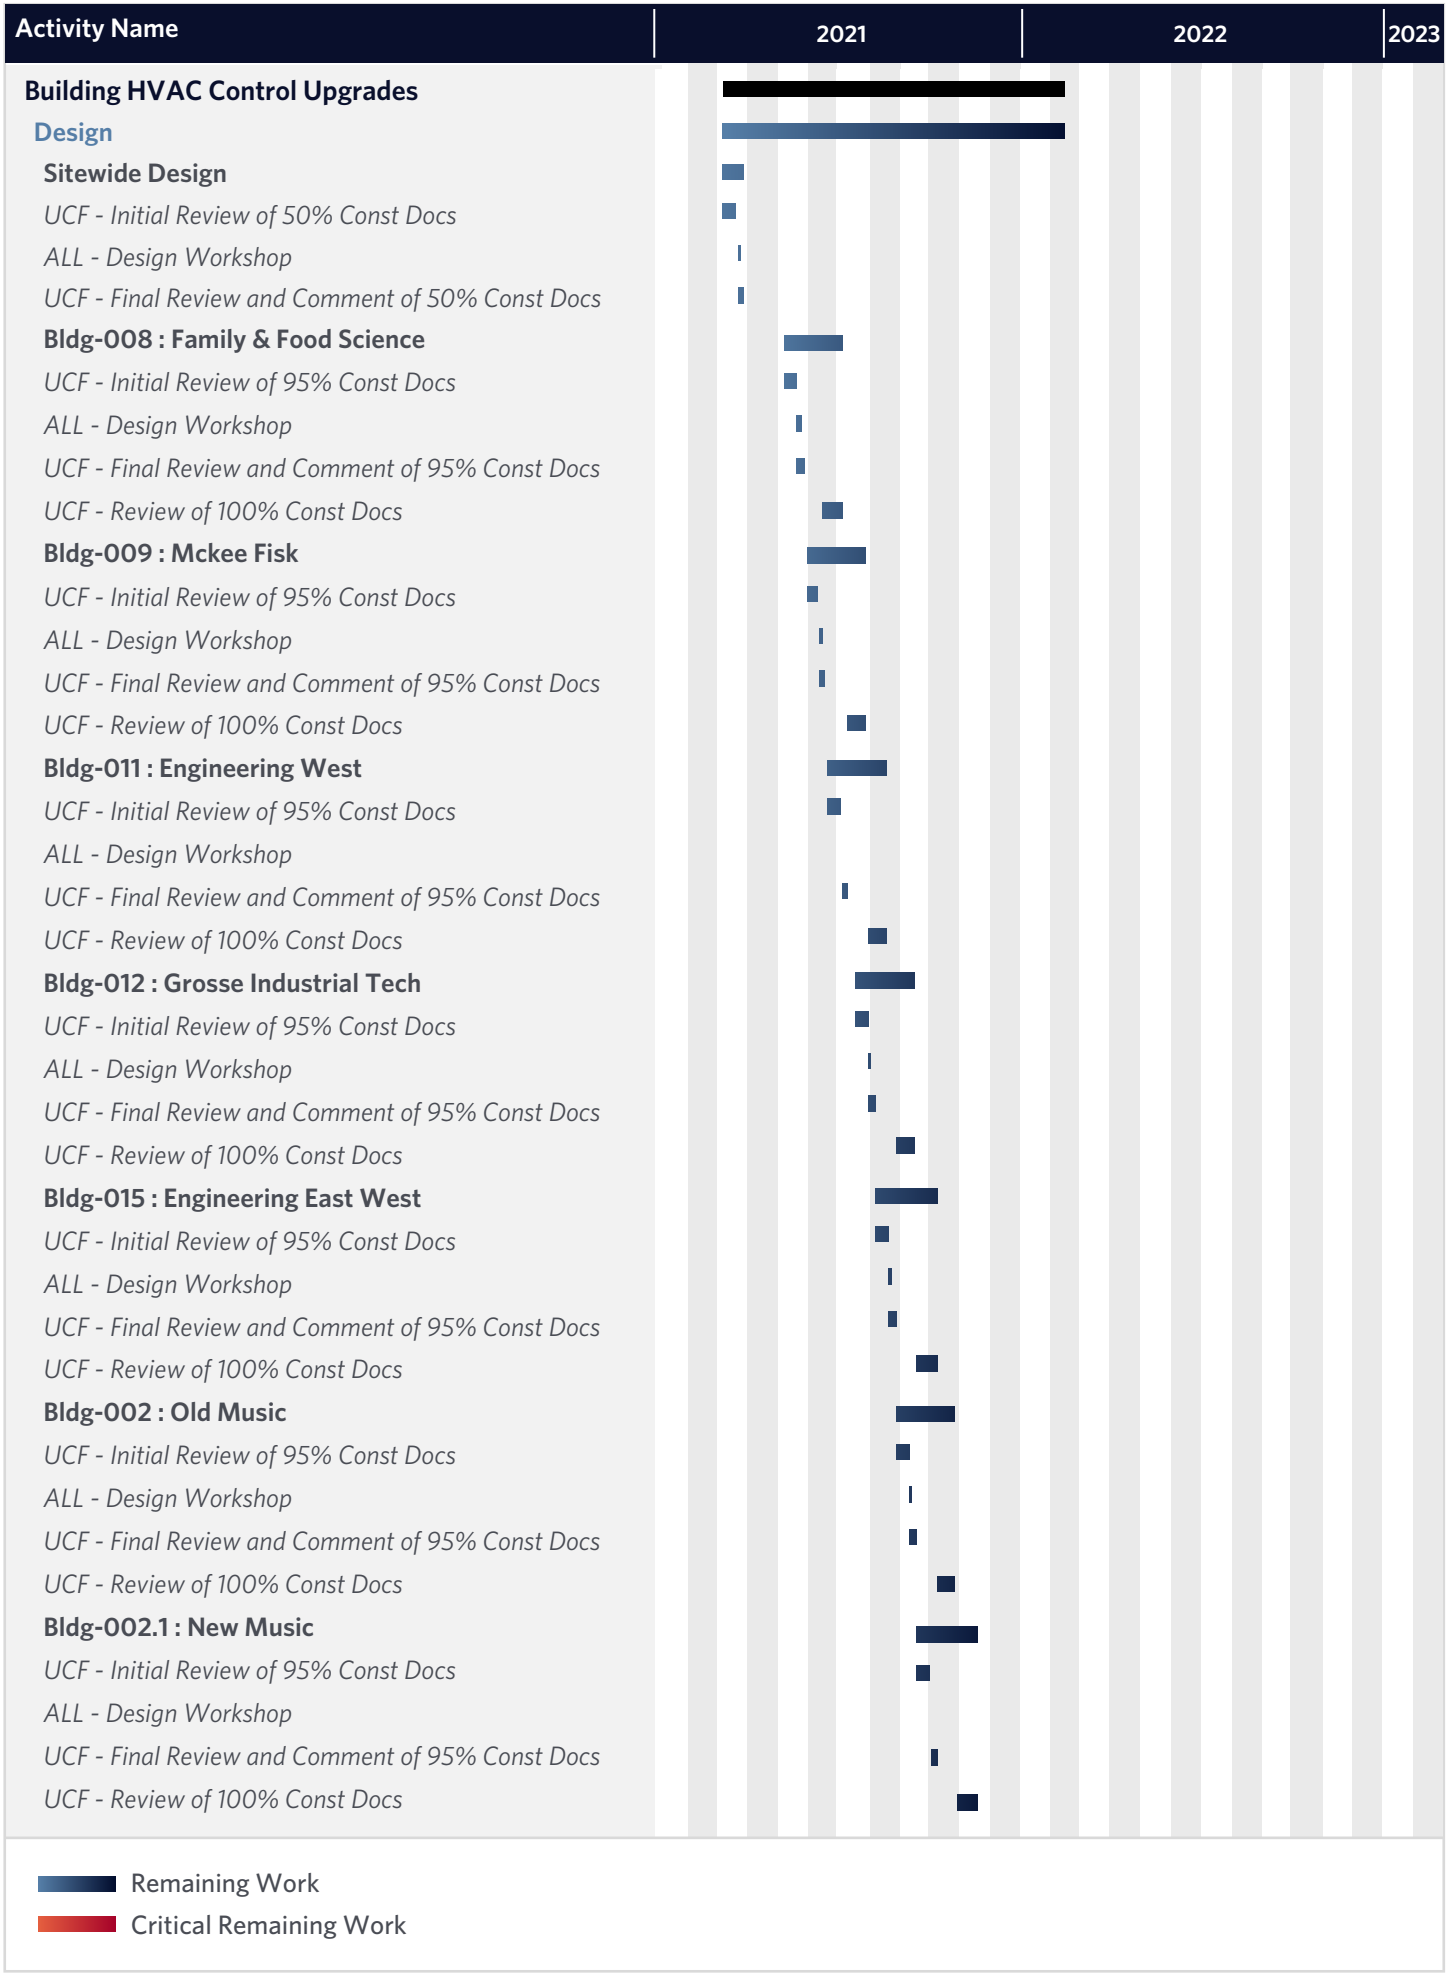
Activity Name
2021
2022
2023
Building HVAC Control Upgrades
Design
Sitewide Design
UCF - Initial Review of 50% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 50% Const Docs
Bldg-008 : Family & Food Science
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Bldg-009 : Mckee Fisk
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Bldg-011 : Engineering West
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Bldg-012 : Grosse Industrial Tech
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Bldg-015 : Engineering East West
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Bldg-002 : Old Music
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Bldg-002.1 : New Music
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Remaining Work
Critical Remaining Work

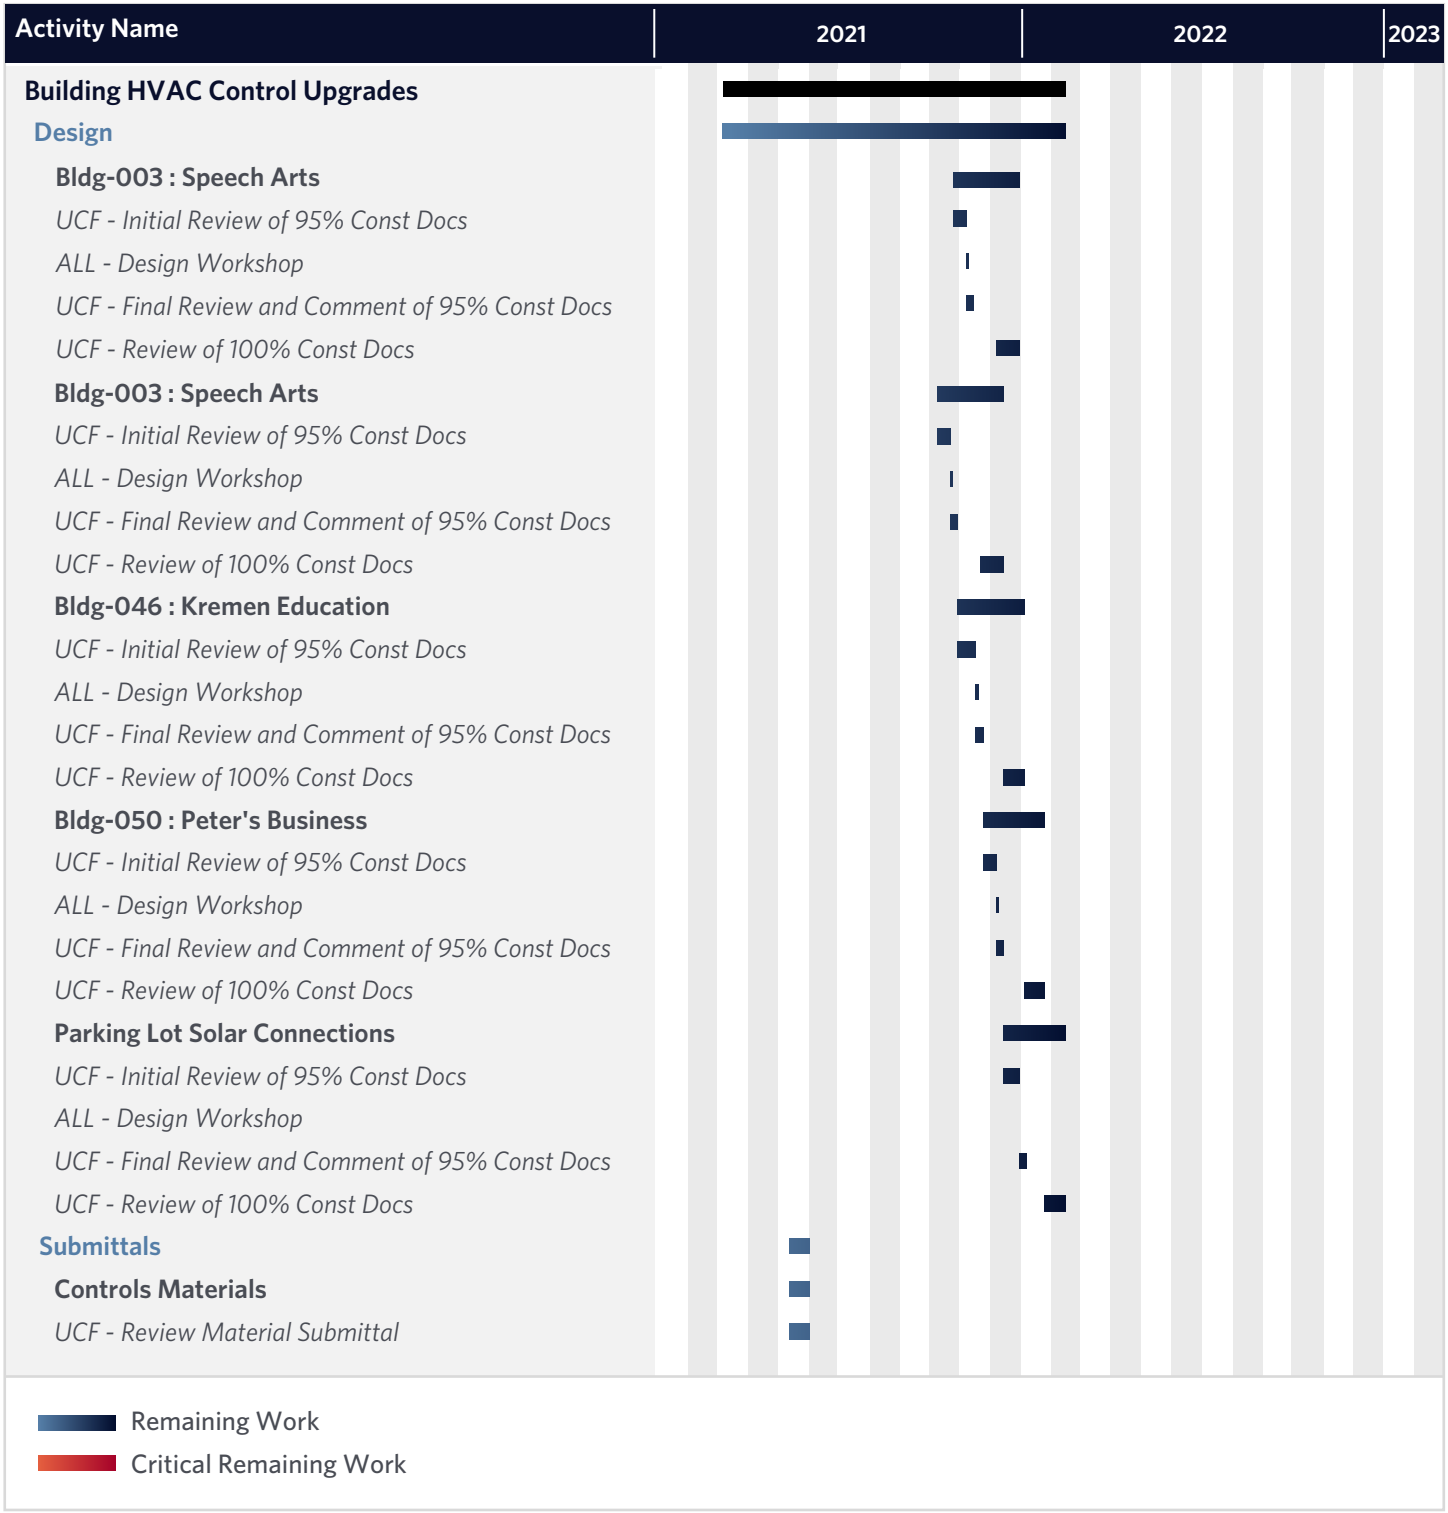
Activity Name
2021
2022
2023
Building HVAC Control Upgrades
Design
Bldg-003 : Speech Arts
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Bldg-003 : Speech Arts
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Bldg-046 : Kremen Education
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Bldg-050 : Peter's Business
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Parking Lot Solar Connections
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
UCF - Review of 100% Const Docs
Submittals
Controls Materials
UCF - Review Material Submittal
Remaining Work
Critical Remaining Work

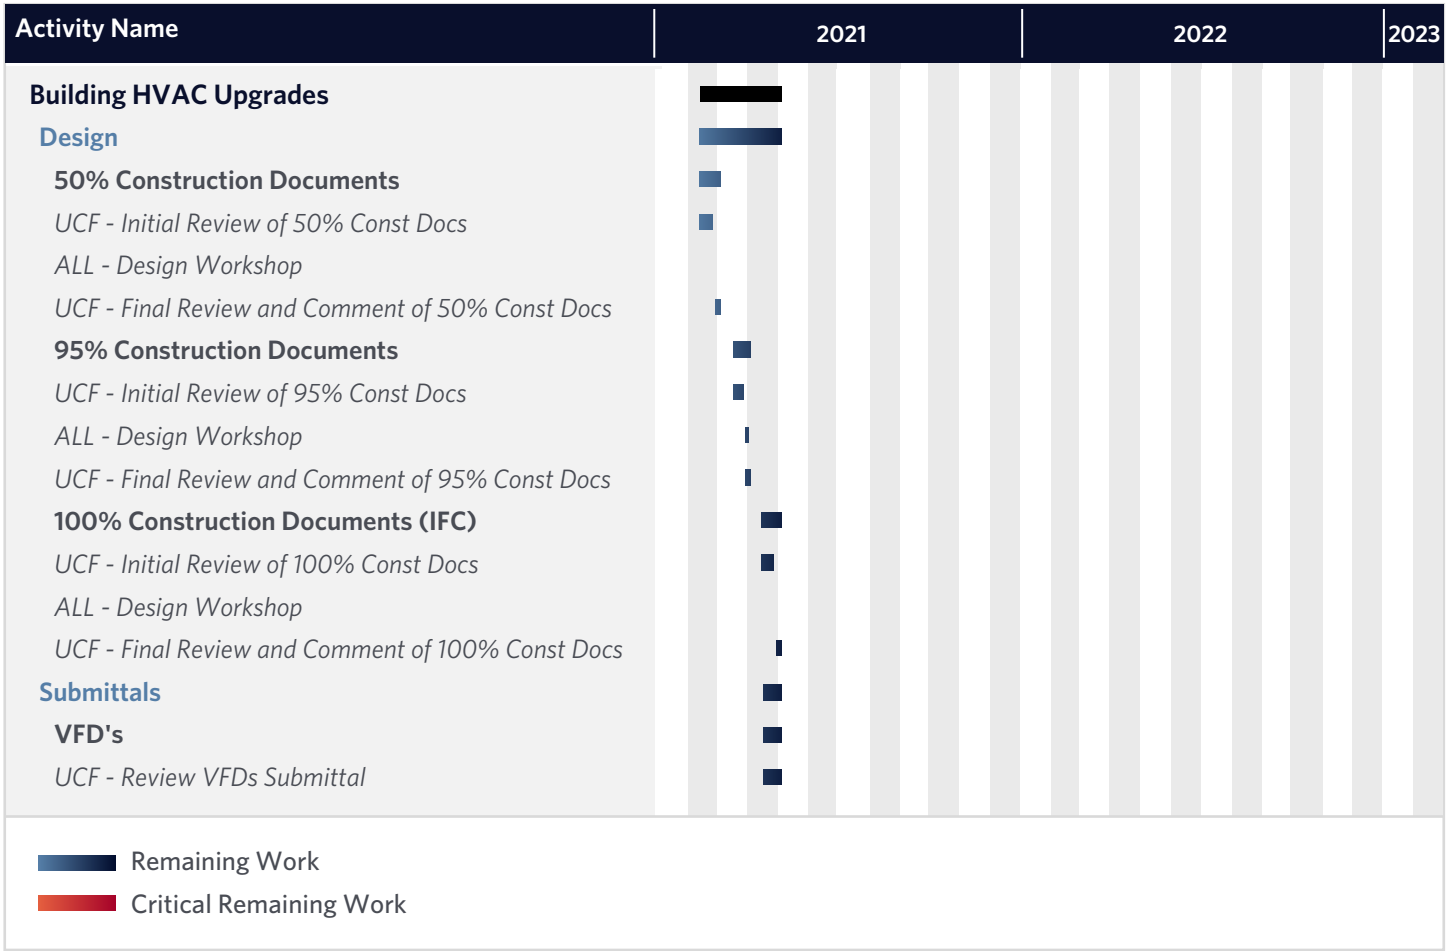
Activity Name
2021
2022
2023
Building HVAC Upgrades
Design
50% Construction Documents
UCF - Initial Review of 50% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 50% Const Docs
95% Construction Documents
UCF - Initial Review of 95% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 95% Const Docs
100% Construction Documents (IFC)
UCF - Initial Review of 100% Const Docs
ALL - Design Workshop
UCF - Final Review and Comment of 100% Const Docs
Submittals
VFD's
UCF - Review VFDs Submittal
Remaining Work
Critical Remaining Work

Activity Name	2021	2022	2023
LED Lighting Improvements			
Design			
50% Construction Documents			
UCF - Initial Review of 50% Const Docs			
ALL - Design Workshop			
UCF - Final Review and Comment of 50%			
95% Construction Documents			
UCF - Initial Review of 95% Const Docs			
ALL - Design Workshop			
UCF - Final Review and Comment of 95% Const Docs			
100% Construction Documents (IFC)			
UCF - Review and Approve of 100% Const Docs			
Submittals			
Light Fixtures			
UCF - Review Lighting Fixtures Submittal			

Remaining Work

Critical Remaining Work
